



Engineering progress curve - 2205 documents, 211,445 h (step at NTP: 173 tender-stage documents, 10,589 h; supplier documents at their VDRL dates) - levelled to the discipline capacities

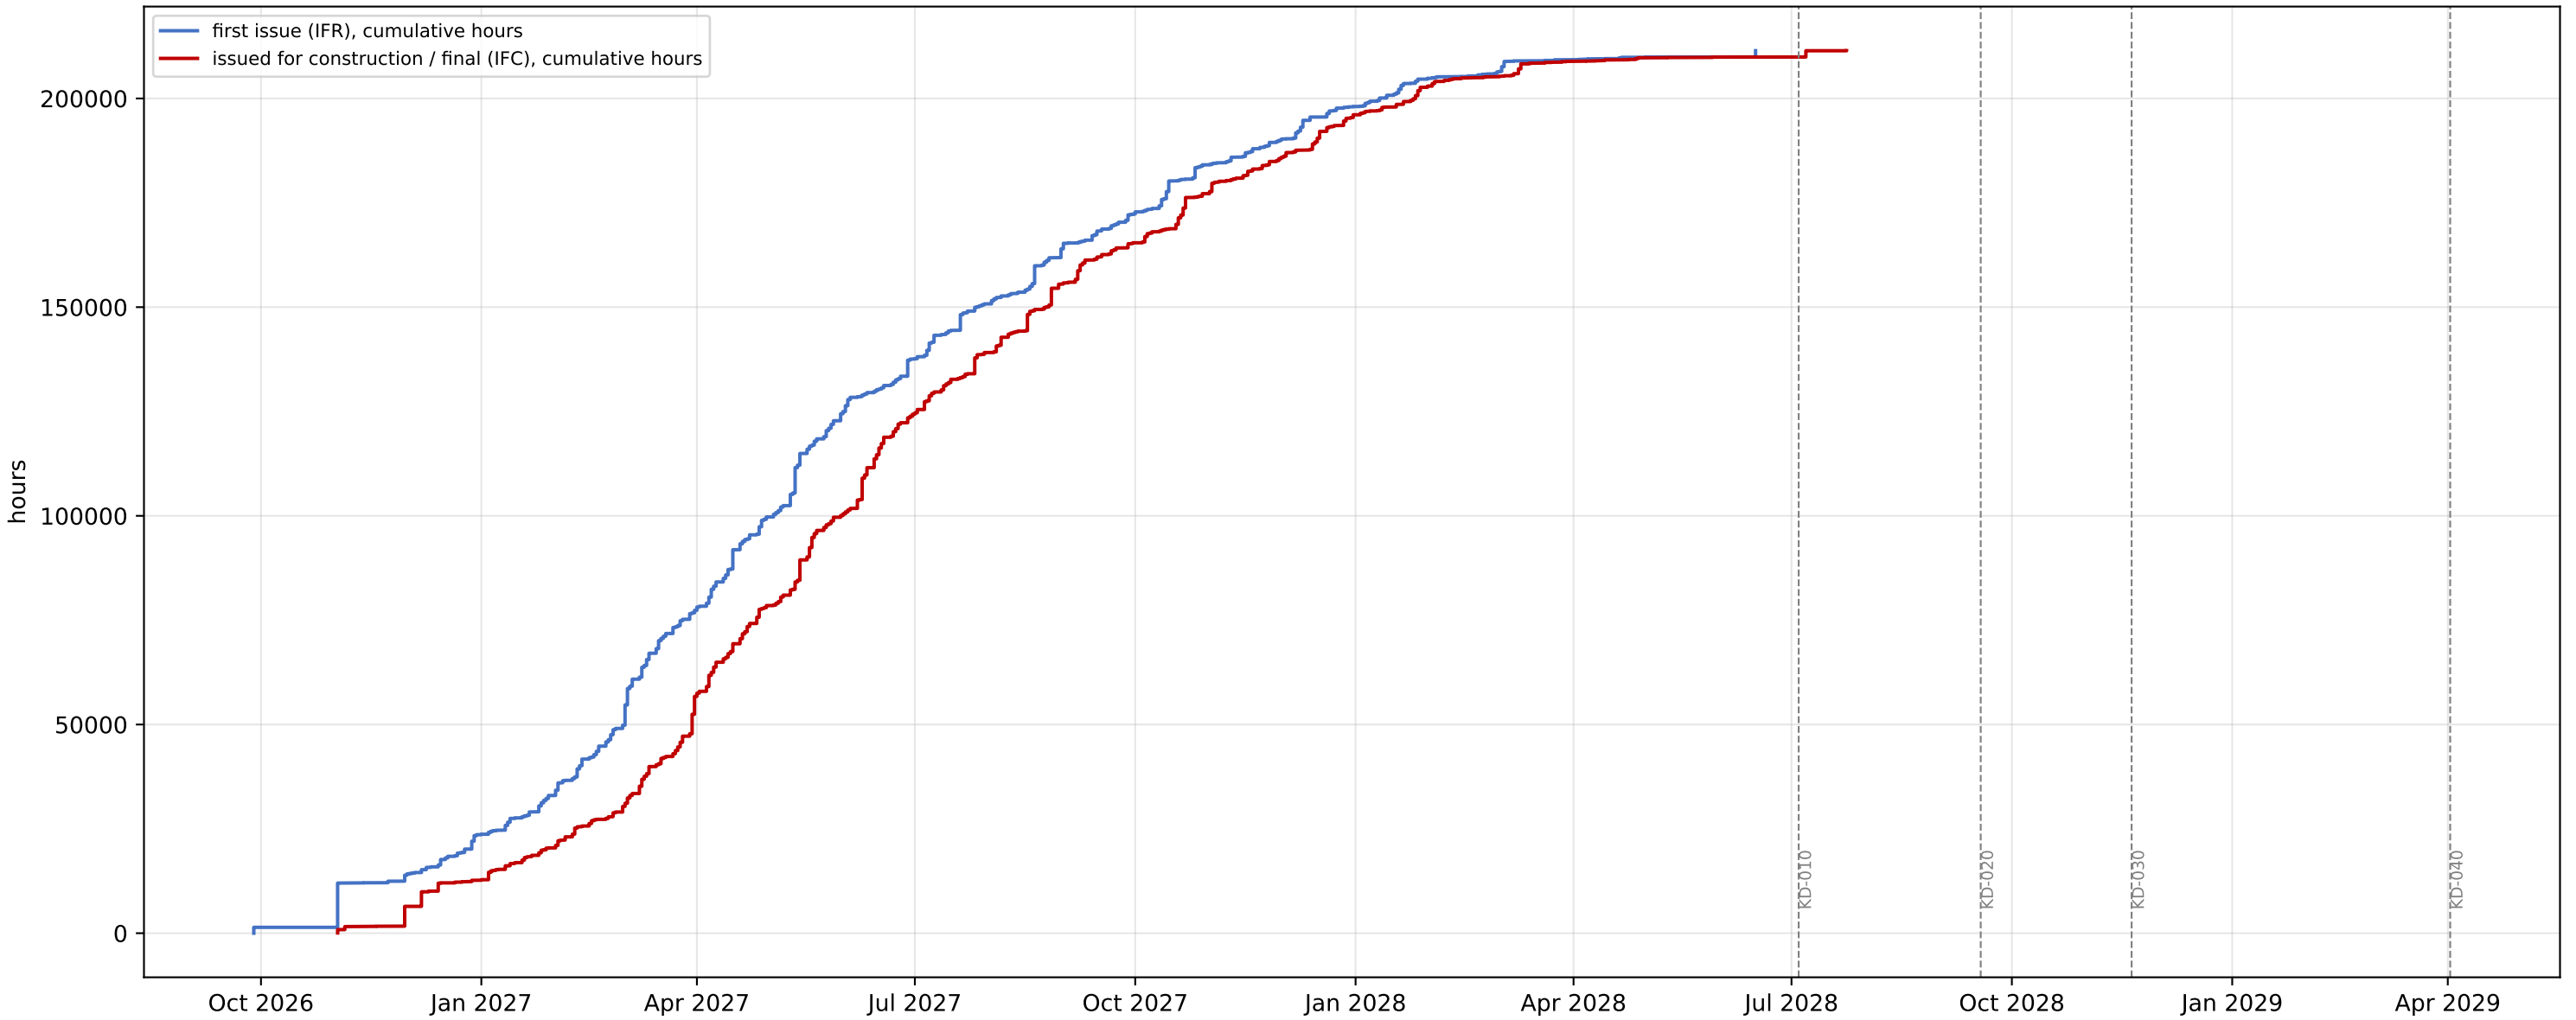


Documents reaching IFC per month

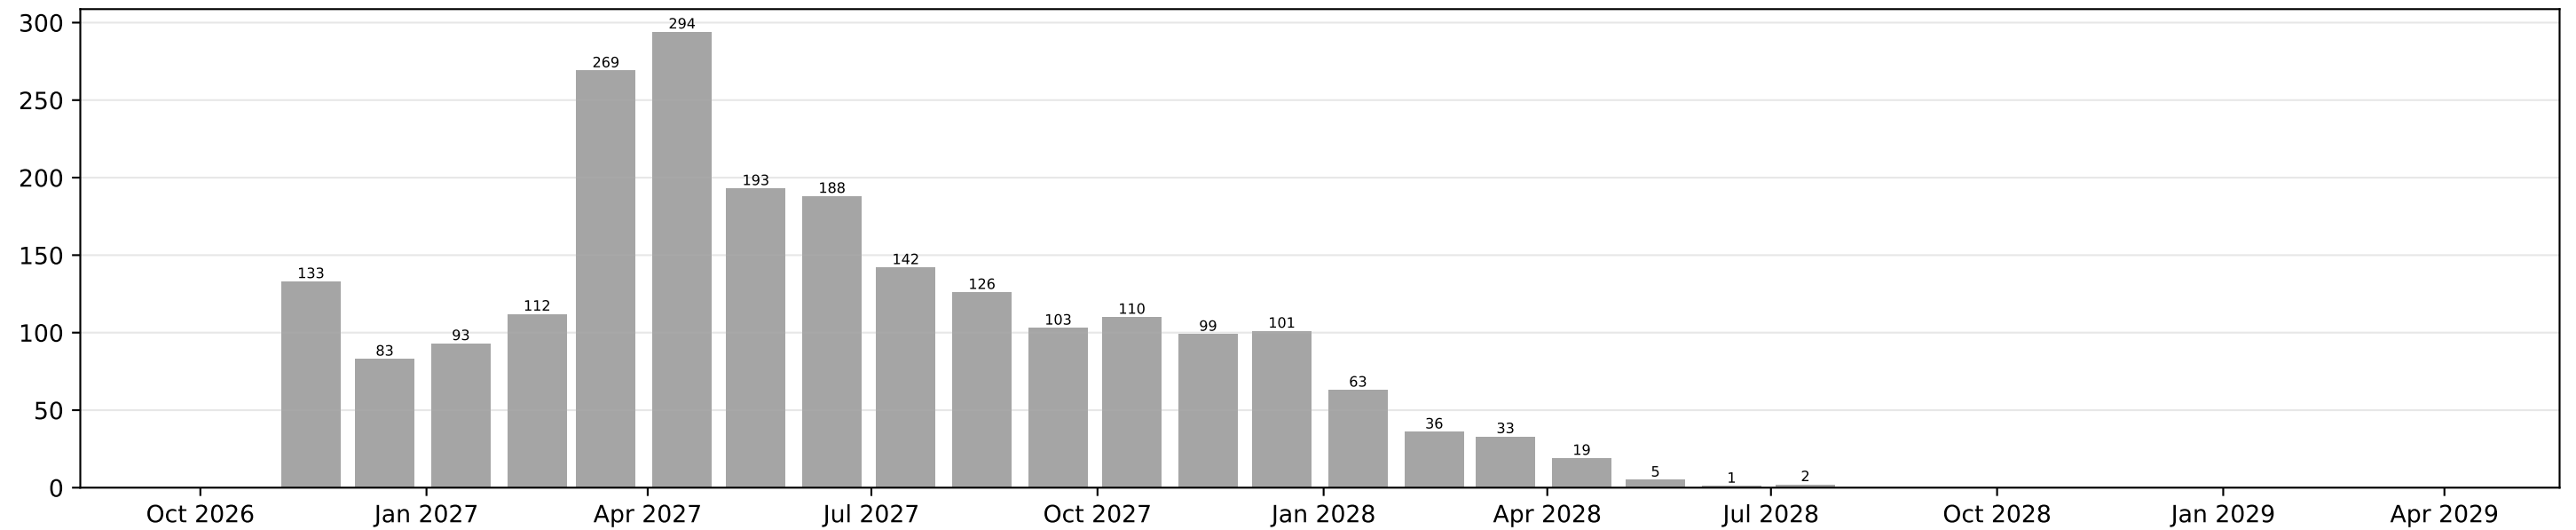


AWP timeline - EWP (blue: first document start to all IFC), PWP (orange: PO to on site), CWP (green: CPM)
| = first need (EWP: CWP start - lead; progressive documents later); numbers = float in working days (EWP: smallest document float); red = late [page 2]




AWP timeline - EWP (blue: first document start to all IFC), PWP (orange: PO to on site), CWP (green: CPM)
| = first need (EWP: CWP start - lead; progressive documents later); numbers = float in working days (EWP: smallest document float); red = late [page 3]

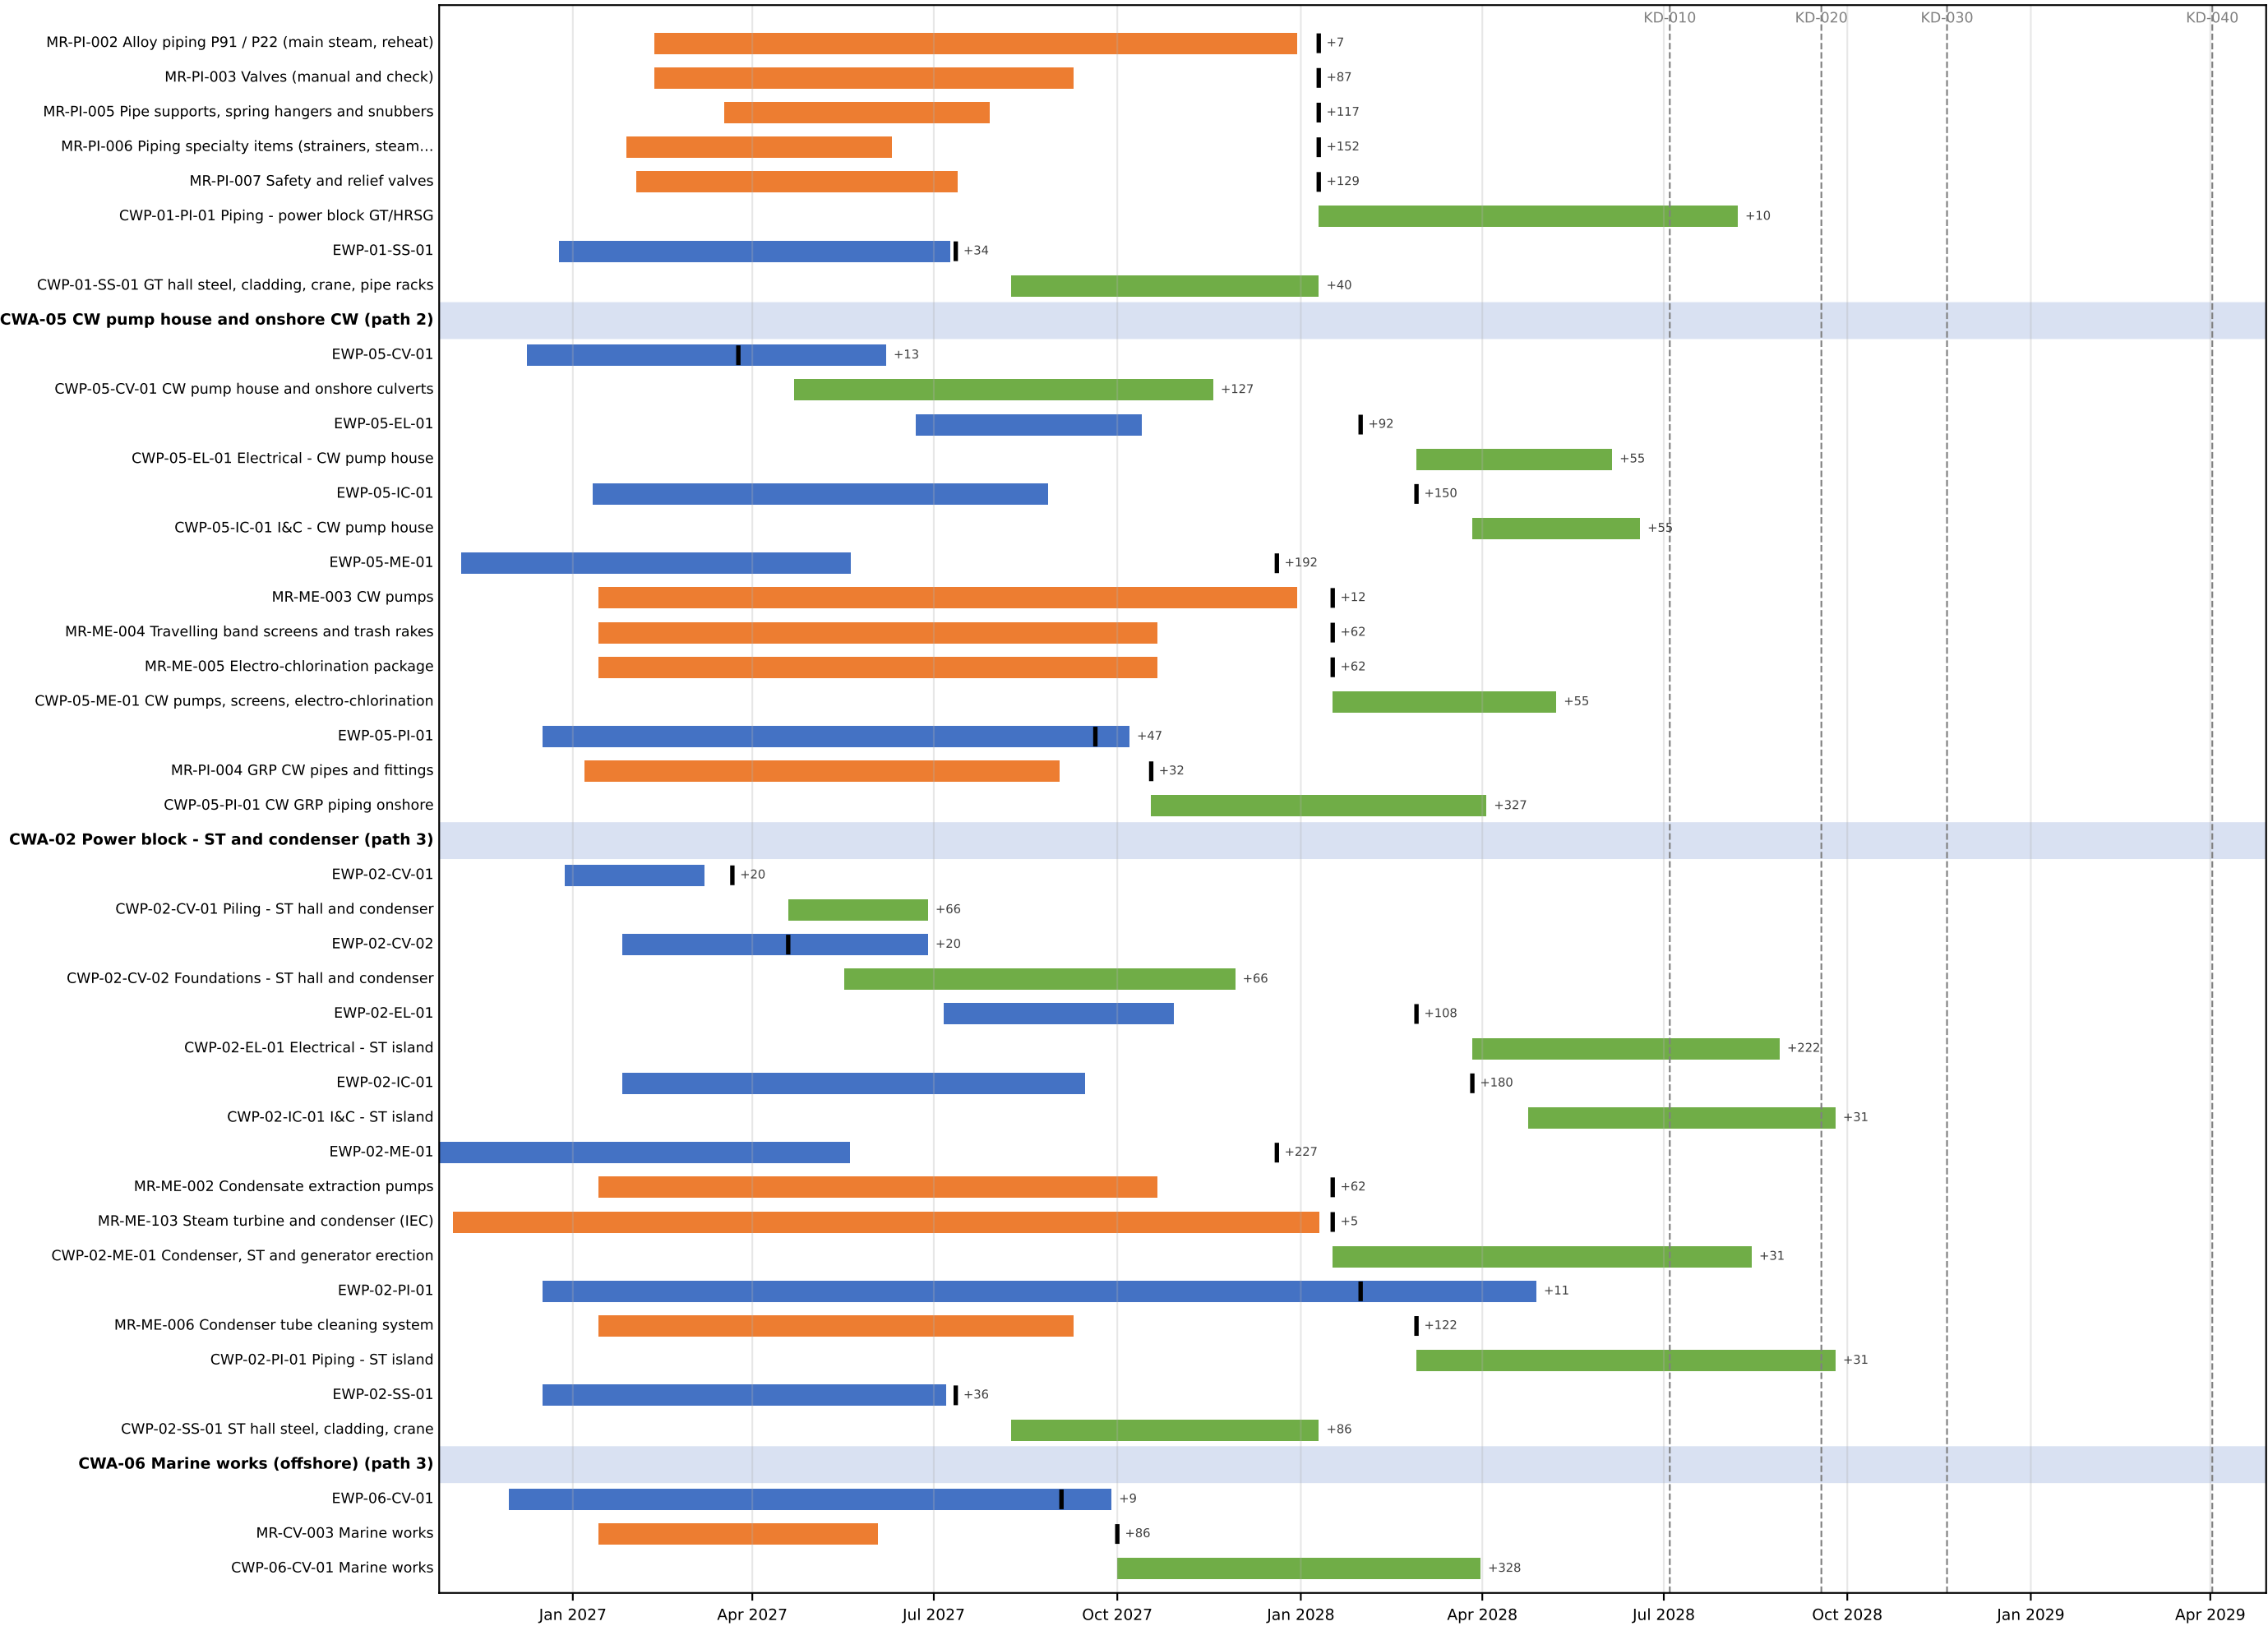

AWP timeline - EWP (blue: first document start to all IFC), PWP (orange: PO to on site), CWP (green: CPM)
| = first need (EWP: CWP start - lead; progressive documents later); numbers = float in working days (EWP: smallest document float); red = late [page 4]

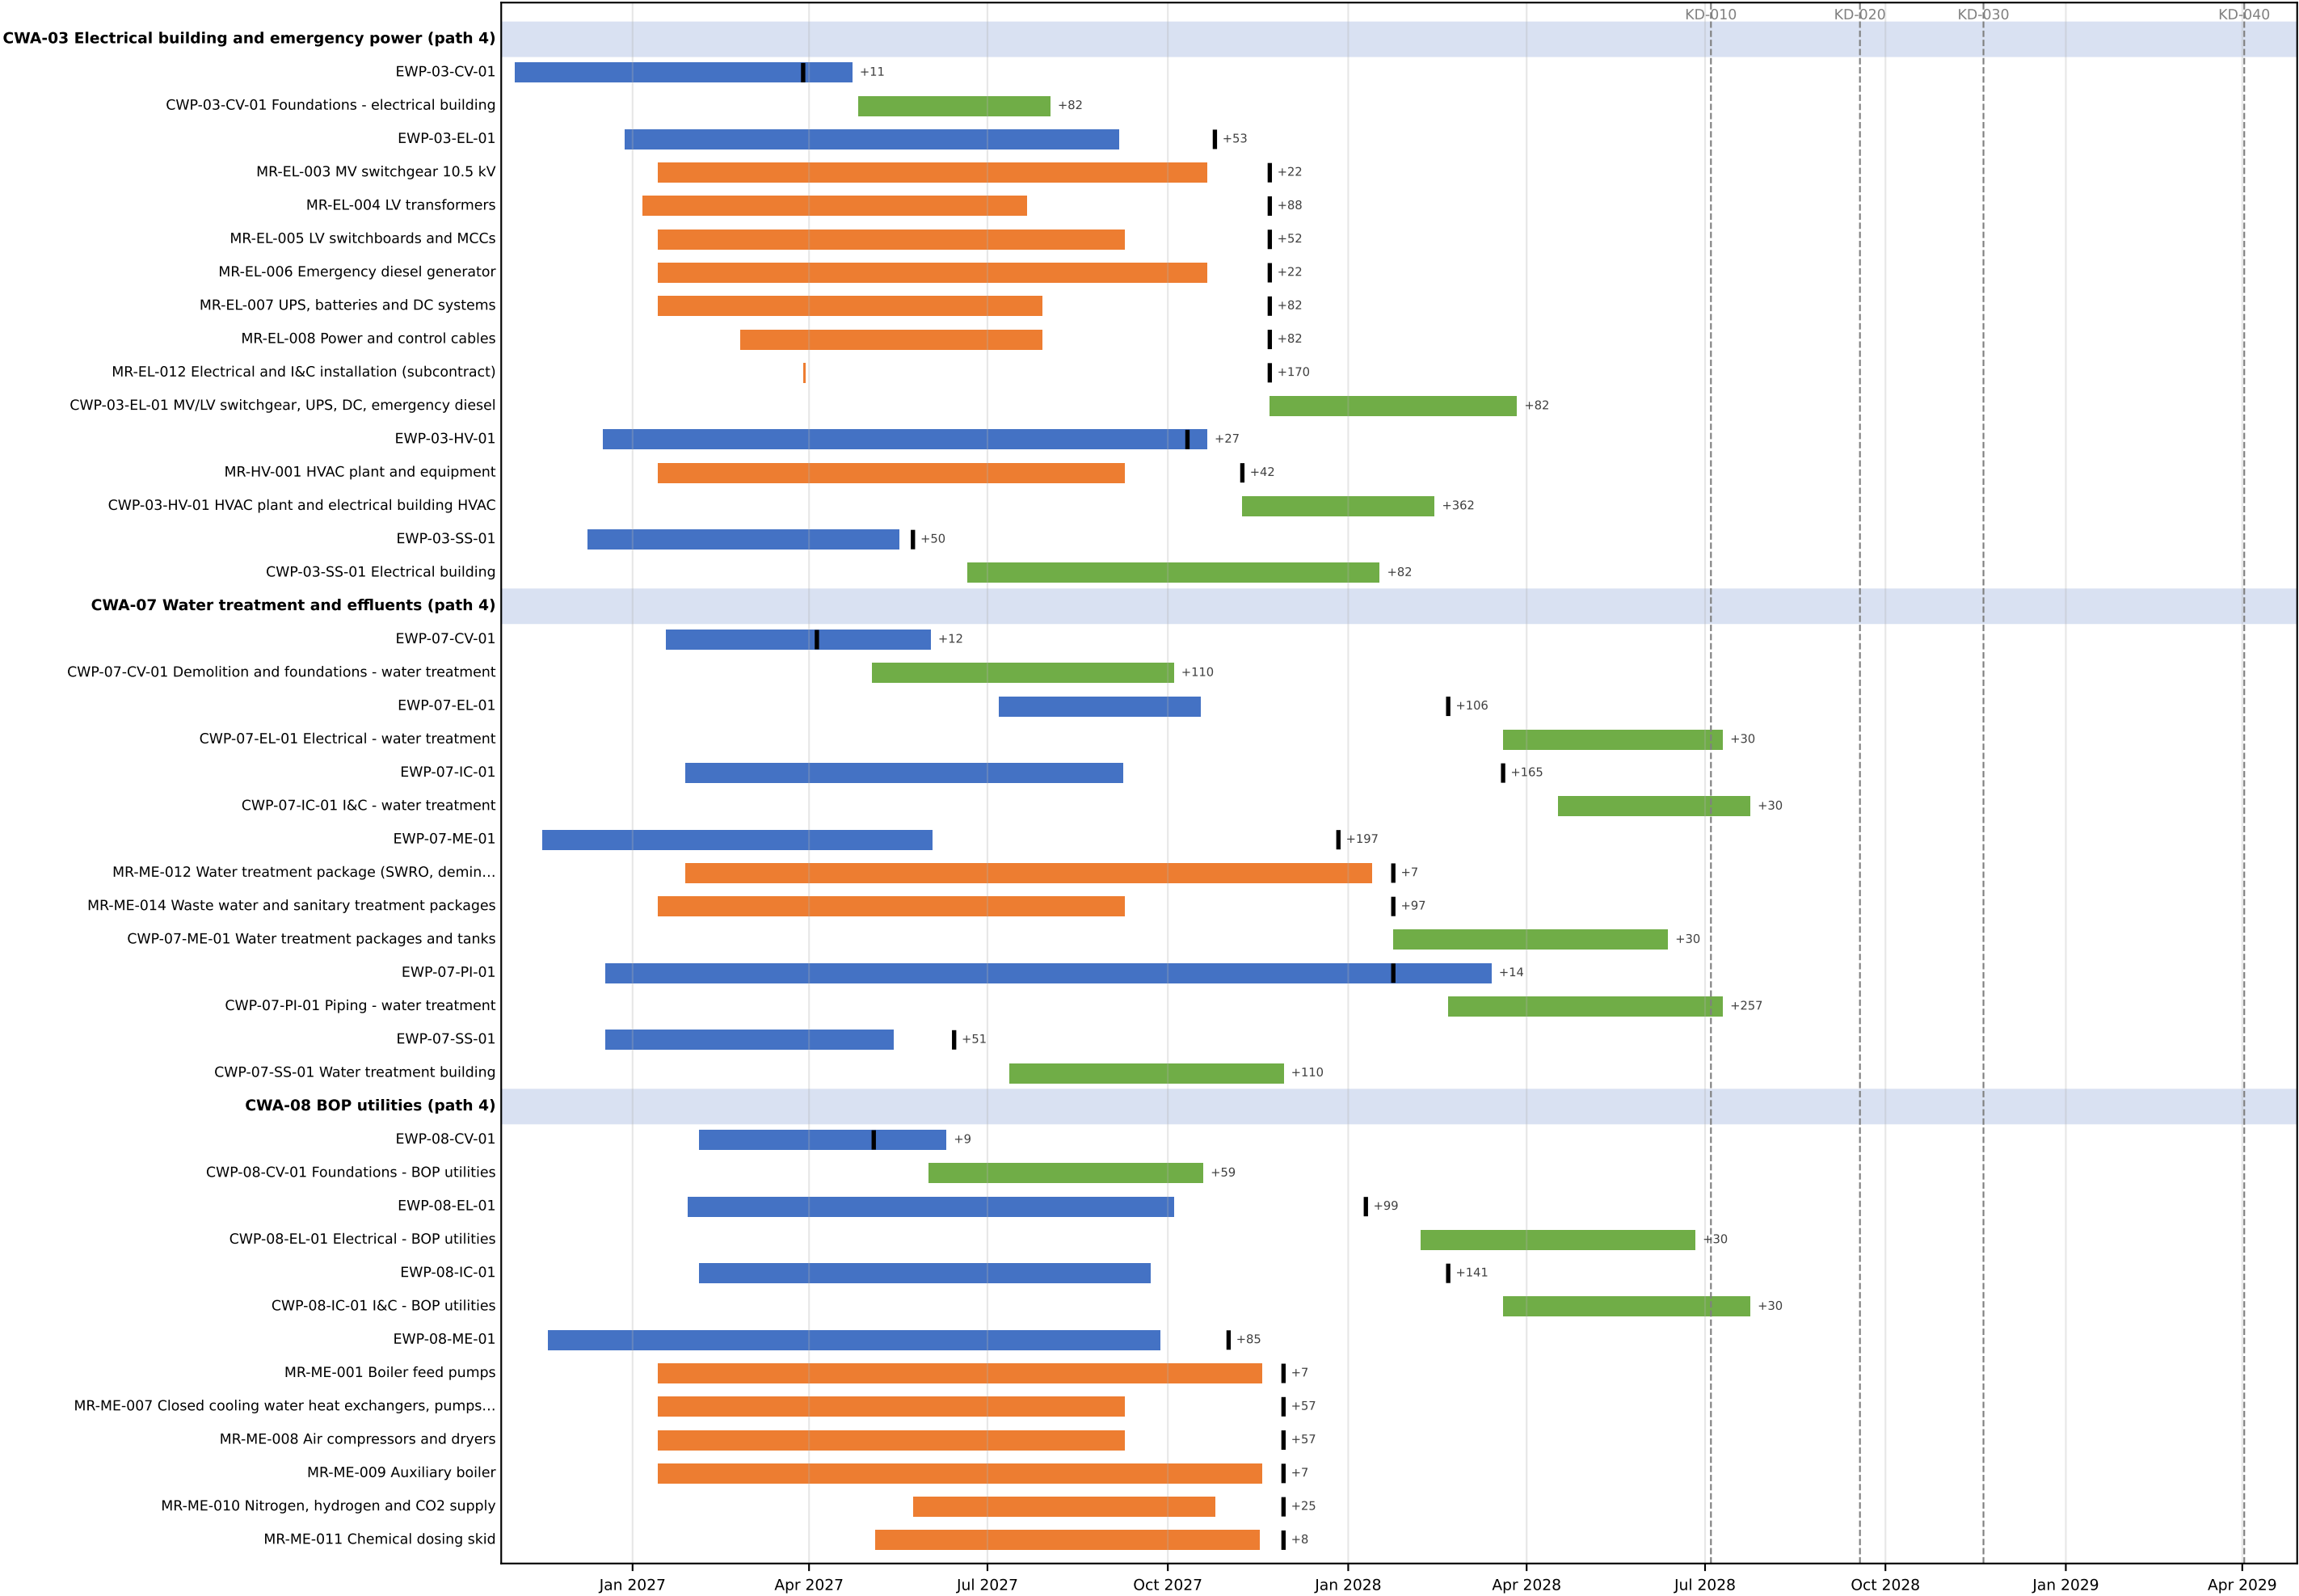

AWP timeline - EWP (blue: first document start to all IFC), PWP (orange: PO to on site), CWP (green: CPM)
| = first need (EWP: CWP start - lead; progressive documents later); numbers = float in working days (EWP: smallest document float); red = late [page 5]

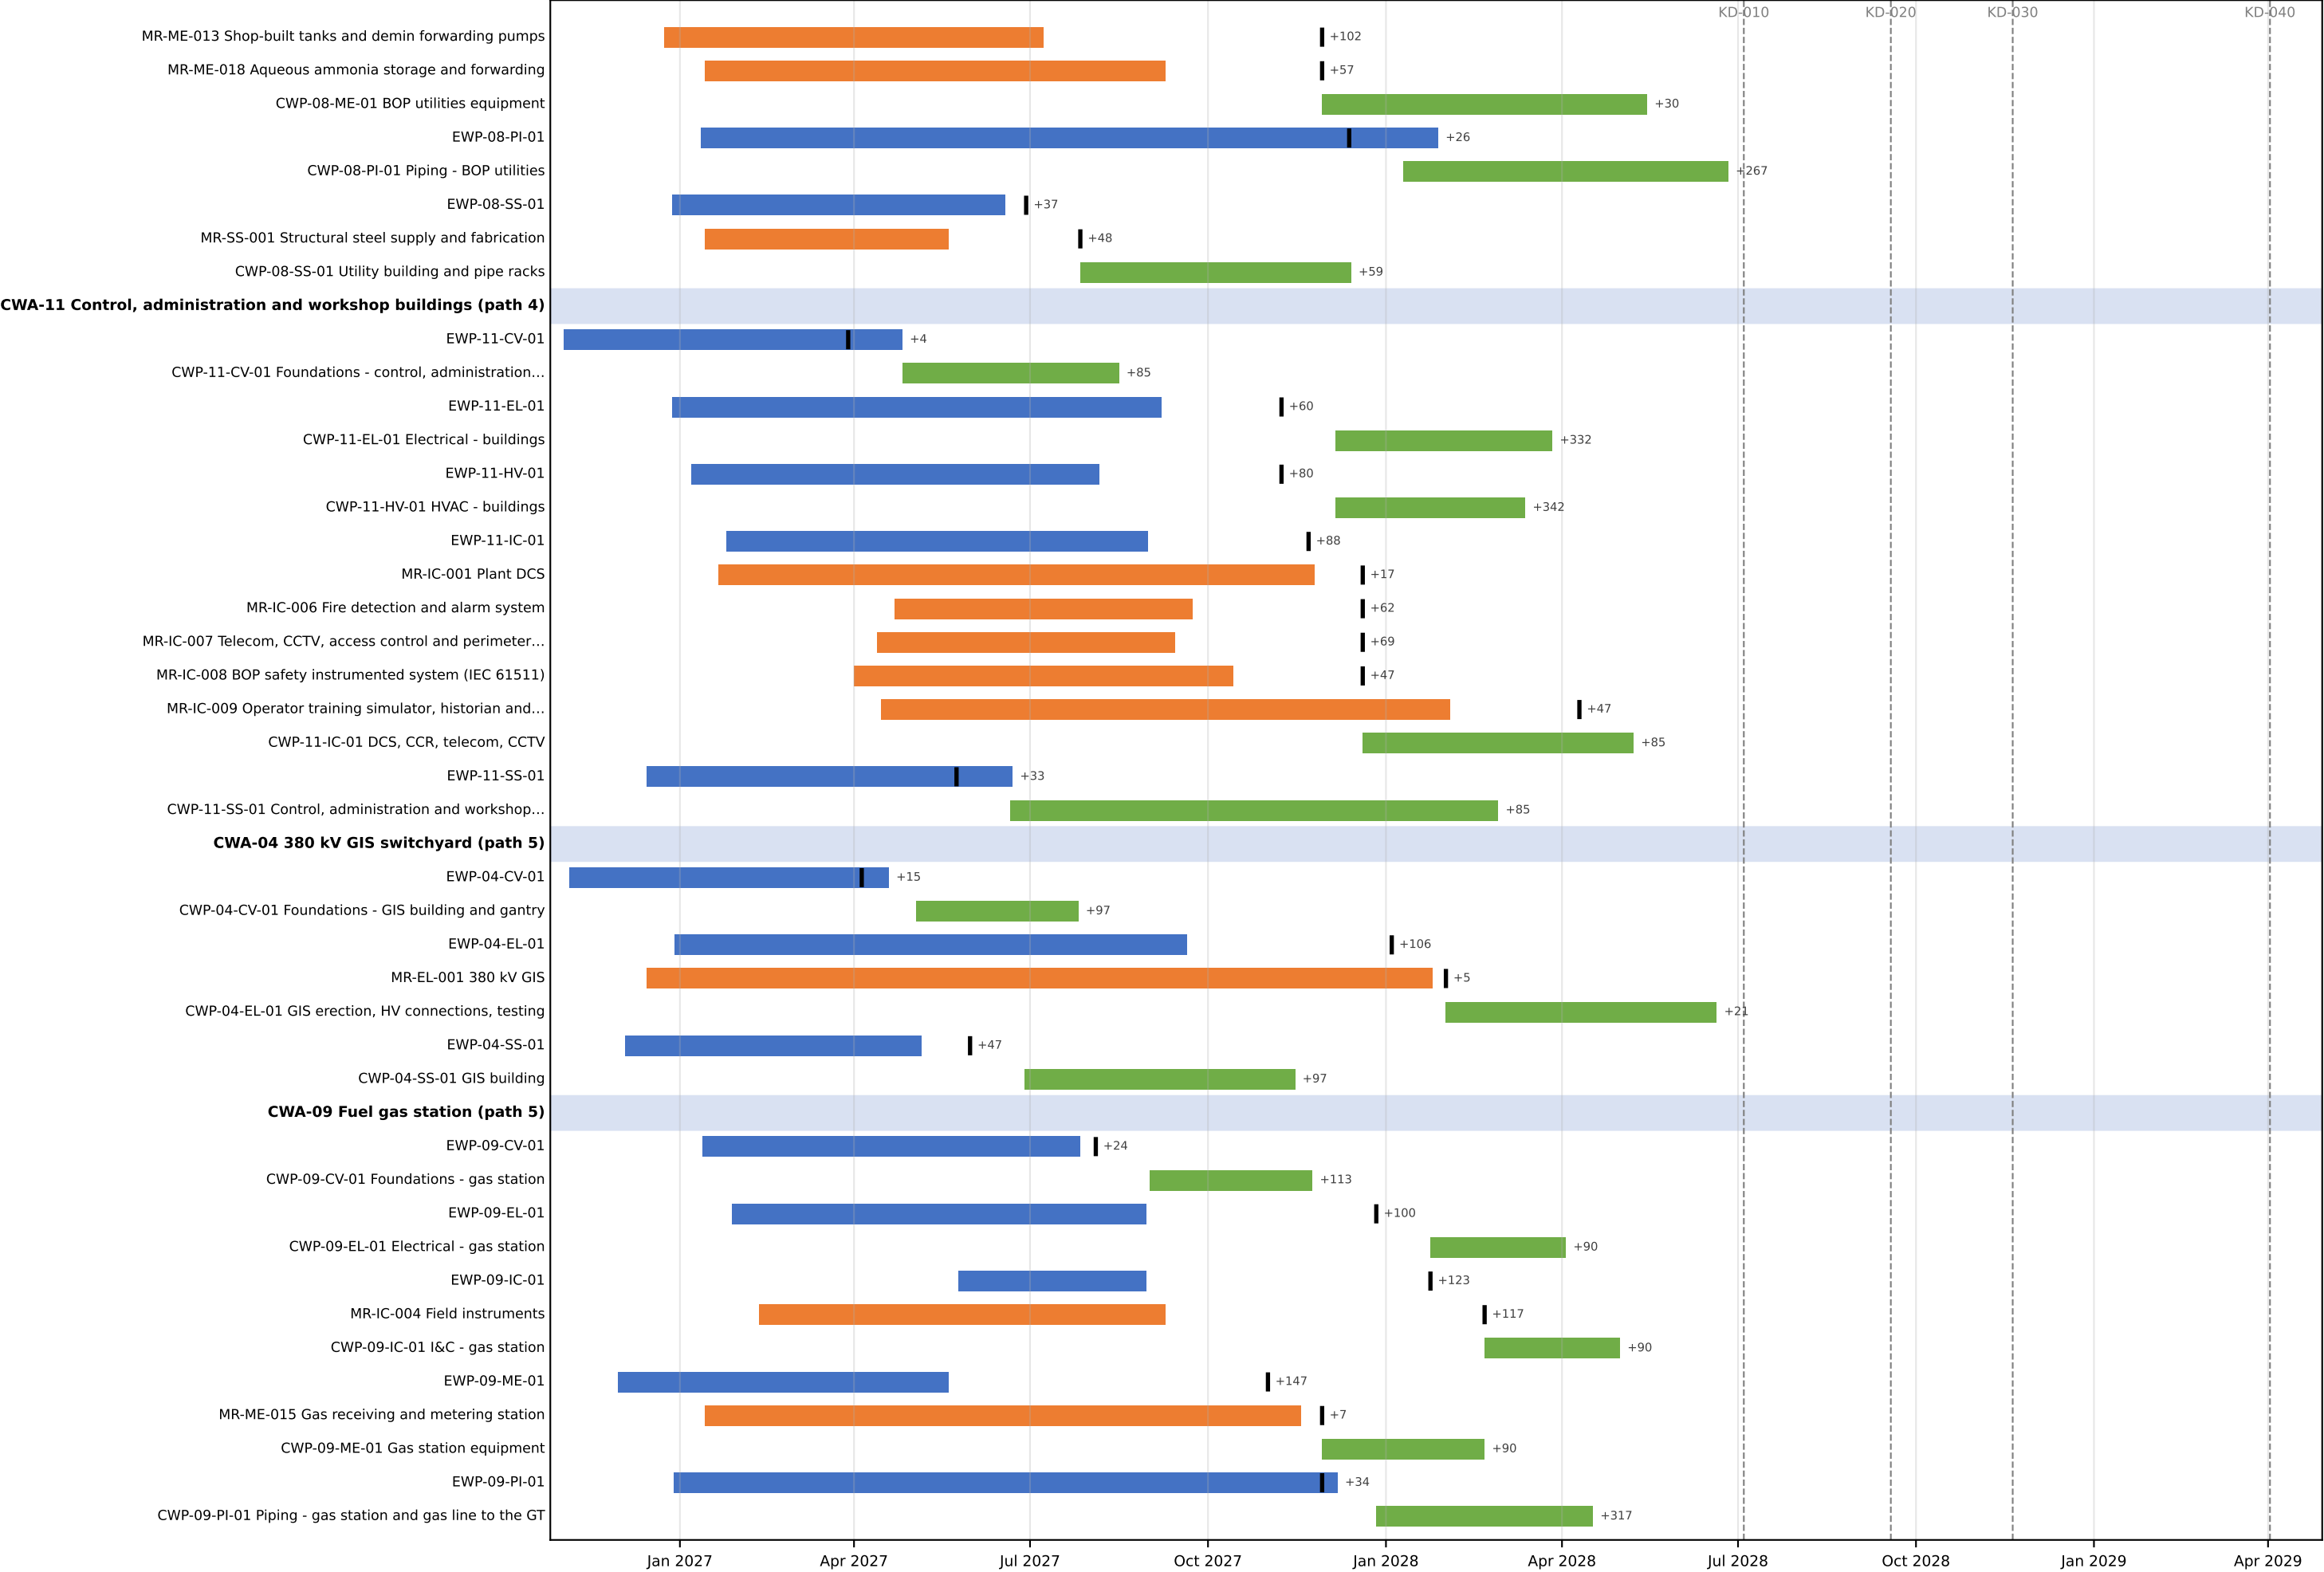

AWP timeline - EWP (blue: first document start to all IFC), PWP (orange: PO to on site), CWP (green: CPM)
| = first need (EWP: CWP start - lead; progressive documents later); numbers = float in working days (EWP: smallest document float); red = late [page 6]

CWA-10 LDO tank farm and unloading (path 5)

EWP-10-CV-01

CWP-10-CV-01 Bund and tank foundations - LDO

EWP-10-EL-01

CWP-10-EL-01 Electrical - LDO

EWP-10-IC-01

CWP-10-IC-01 I&C - LDO

EWP-10-ME-01

MR-ME-016 LDO unloading and forwarding / treatment skids

MR-ME-017 LDO storage tanks (field-erected, API 650)

CWP-10-ME-01 LDO tanks and skids

EWP-10-PI-01

CWP-10-PI-01 Piping - LDO

KD-010 KD-020 KD-030 KD-040

